Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	9 September 2026
Team ID	Individual
Name	Boyapati Rishi
Project Name	Digital Metro Ticket Booking System using ServiceNow
Maximum Marks	4 Marks

Product Backlog, Sprint Schedule, and Estimation

The product backlog below is prepared for the Digital Metro Ticket Booking System using ServiceNow.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	**Requirement Analysis & Planning**	US-01	As a passenger, I can access a standardized Metro Ticket Booking catalog item through ServiceNow.	2	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-1	**Service Catalog**	US-02	As a passenger, I can provide Source, Destination, Passenger Type, and Number of Tickets while booking.	3	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-1	**Station Details Mapping**	US-03	As the system, I can validate and map the selected source and destination stations for ticket processing.	3	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-2	**Fare Calculation**	US-04	As the system, I can automatically calculate the fare using journey, passenger, and ticket quantity details.	3	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-2	**Booking Processing**	US-05	As a passenger, I can receive a booking result containing the calculated fare after submitting valid details.	3	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-3	**Digital Ticket**	US-06	As a passenger, I can receive a digital metro ticket containing my journey and fare information.	3	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-3	**QR Code Integration**	US-07	As the system, I can generate a QR code associated with the digital metro ticket.	2	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-3	**Ticket Tracking**	US-08	As a passenger, I can view the status and details of my booking and generated ticket.	2	Medium	Jonnalagadda Sai Sri Poornima Lahari
Sprint-4	**UAT & Validation**	US-09	As an administrator, I can test booking, fare calculation, ticket generation, and QR-code behavior before deployment.	2	High	Jonnalagadda Sai Sri Poornima Lahari
Sprint-4	**Deployment & Handover**	US-10	As an administrator, I can deploy the validated ServiceNow configuration and confirm the complete ticket-booking flow.	2	High	Jonnalagadda Sai Sri Poornima Lahari

Sprint Planning & Project Tracker

Sprint Schedule

Four planned sprints organize the project work. Actual dates can be entered during execution.

Sprint	User Stories	Story Points	Planned Scope
Sprint-1	US-01 to US-03	8	Requirement analysis, Service Catalog, booking variables, and station details mapping.
Sprint-2	US-04 to US-05	6	Automated fare calculation and booking processing.
Sprint-3	US-06 to US-08	7	Digital ticket generation, QR-code integration, and ticket tracking.
Sprint-4	US-09 to US-10	4	UAT, validation, deployment, and final handover.

Project Tracker

Sprint	Total Story Points	Status	Sprint Start Date	Sprint End Date (Planned)	Sprint Release Date (Actual)
Sprint-1	8	Planned	TBD	TBD	TBD
Sprint-2	6	Planned	TBD	TBD	TBD
Sprint-3	7	Planned	TBD	TBD	TBD
Sprint-4	4	Planned	TBD	TBD	TBD

Velocity

Velocity represents the amount of work completed by the team during a sprint, measured in story points. This project has **25 planned story points** across four sprints.

Planned average velocity = 25 story points ÷ 4 sprints = 6.25 story points per sprint.


Actual velocity should be calculated after each sprint using the story points actually completed. No actual completion values have been assumed.

Planning Notes

The sprint structure follows the execution roadmap: Catalog Form Setup → Fare Logic Script → QR Code Integration → Station Details Mapping → UI Pages → UAT & Deployment.

Burndown Chart

A burndown chart is a graphical representation of work left to do versus time. For this project, it tracks remaining story points across the four planned sprints.

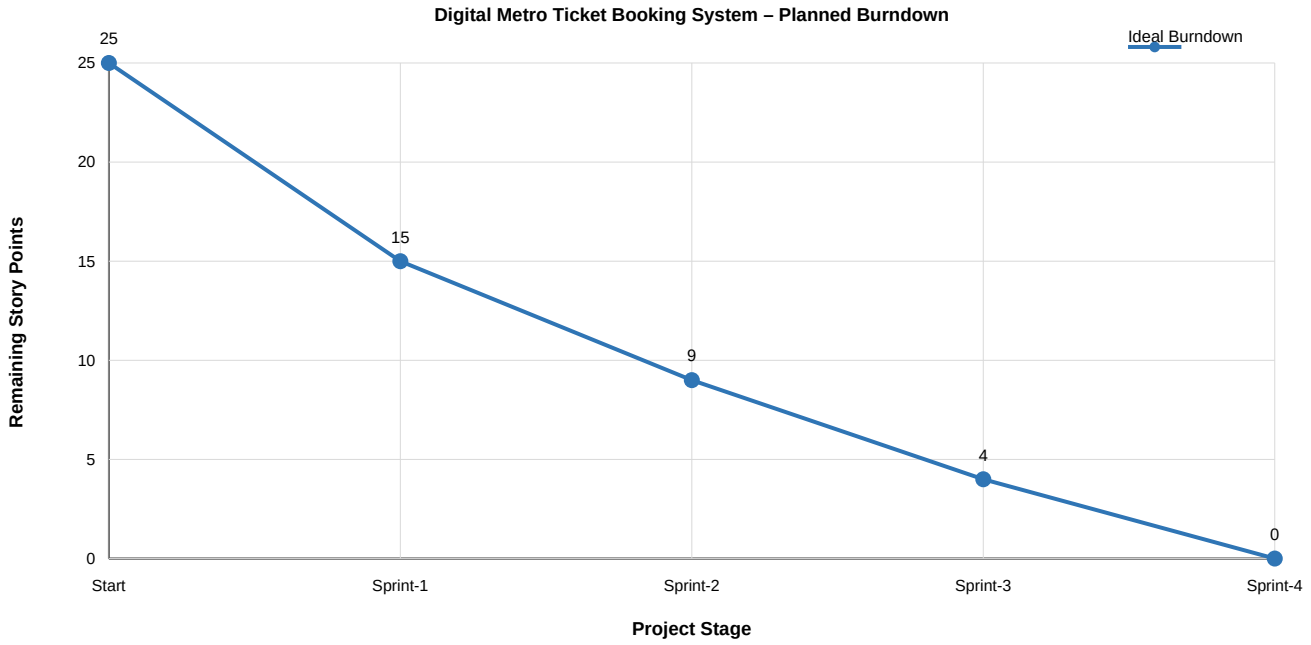

How to interpret the chart

• The X-axis represents the project stages from project start through Sprint-4.

• The Y-axis represents remaining work in story points.

• The ideal line starts at 25 story points and decreases to 0.

• Actual remaining work should be updated during execution using the story points still incomplete.

• If actual work remains above the ideal line, the project may be behind the planned schedule.

Planned Burndown Values

Stage	Ideal Remaining Story Points	Actual Remaining Story Points
Project Start	25	TBD
End of Sprint-1	17	TBD
End of Sprint-2	11	TBD
End of Sprint-3	4	TBD
End of Sprint-4	0	TBD

Project Planning Details

Project Objective

To digitize metro ticket booking through ServiceNow Service Catalog by standardizing the booking form, automating fare calculation, mapping station details, generating digital tickets with QR codes, and maintaining booking data for tracking and operational insights.

Planned Work by Project Area

Project Area	Planned Work
Service Catalog	Create the Metro Ticket Booking catalog item and configure Source, Destination, Passenger Type, and Number of Tickets variables.
Station Details Mapping	Configure station information and use source/destination selections for route and fare processing.
Fare Logic	Implement automated fare calculation based on the configured journey, passenger category, and ticket quantity.
Digital Ticket	Generate a digital ticket containing the journey, passenger, quantity, and fare details.
QR Code Integration	Generate and display a QR code associated with the digital ticket for convenient access and validation.
UI Pages	Provide a clear interface for viewing booking results, digital ticket details, and QR-code information.
Testing & UAT	Test form submission, validation, station mapping, fare calculation, ticket generation, QR-code behavior, and end-to-end workflow.
Deployment	Complete final validation and deploy the configured ServiceNow solution for project use.

Acceptance Criteria

- Passenger can submit the Metro Ticket Booking request through the Service Catalog.
- The catalog captures Source, Destination, Passenger Type, and Number of Tickets.
- The selected station details are validated and used for fare processing.
- Fare is calculated automatically using the configured fare logic.
- A digital ticket is generated with the required journey and fare information.
- A QR code is generated and displayed with the digital ticket.
- The passenger can view the booking/ticket information after successful processing.
- The complete solution passes UAT and the final configured workflow is ready for deployment.

Project Planning Summary

Item	Project-Specific Details
Project Name	Digital Metro Ticket Booking System using ServiceNow
Team	Individual
Team Member	Boyapati Rishi
Platform	ServiceNow
Planned User Stories	10
Planned Story Points	25
Planned Sprints	4
Primary Users / Stakeholders	Passengers, Station Managers, Metro Operations Team, IT Administrators
Core Features	Service Catalog, Fare Calculation, Station Mapping, Digital Ticket, QR Code, UI Pages, UAT & Deployment
